

title: G · Executive One-Pager description: A single-page brief for evaluator committee chairs and senior officials — the ABC math, milestone Gantt, eight differentiators, and top three risks in one page. hide:

- toc

G · Executive One-Pager

!!! info “How this paper is used” Papers **A / B / C / D / E / F** run 15–75 KB each. This paper is deliberately **one page** — for evaluator committee chairs, DepEd senior officials, and anyone who needs the argument in 90 seconds, not 90 minutes. Every number carries a pointer to the detailed paper.

The bid, in one paragraph

DepEd’s Human Resources Information System (project **2026C-ICTS2-002-B5-CB-034**) is a **1 M+ employee, 11-module** system to be delivered in **365 days** at an ABC of **PHP 500 M**. This analysis models delivery under **two deployment options** — on-premises at DepEd Central Office (**PHP 421 M**, 15.7 % headroom) or public cloud on GovCloud PH / AWS Manila (**PHP 359 M**, 28.2 % headroom). Both use the same **69-FTE peak team at 2026 PH-market rates** and both ship the same eight **value-added components** at no incremental cost. The choice between them is a decision framework at inception (M1), not a bid-time commitment.


- **The numbers**
 - **ABC** — PHP 500 M
 - **Option A · On-prem** — PHP 421 M · Headroom 15.7 %
 - **Option B · Cloud** — PHP 359 M · Headroom 28.2 %
 - **1 M+ employees** across CO / RO / SDO / District / Schools
 - **365 days** to final acceptance · **8 milestones** · **99 % uptime**
 - **P1** 1 h resp / 24 h res · **P2** 2 h / 48 h · **P3** 4 h / 5 d · **P4** 1 d / next release
 - **11 modules**, of which 3 are detailed in the TOR
 - **28 recruitment reports**, 9 regulator integrations
 - **69 FTE peak** (M3–M6), 17.5 FTE warranty year
- **The approach**
 - **Modular monolith** in PostgreSQL 16, extracted to services only where load demands (Payroll first)
 - **Two deployment options, both PBD-compliant:**
 - **Option A** — on-prem at DepEd Central Office + colo DR (PHP 101 M CAPEX)
 - **Option B** — GovCloud PH or AWS Manila (PHP 3.96 M / mo OPEX)
 - **Keycloak** for OAuth2/OIDC/MFA · **BPMN engine** for workflow · **OpenSearch** for retrieval and audit
 - **Offline-first PWA** with CRDT sync for low-connectivity schools
 - **In-house team** (SCC 7 forbids subcontracting), Filipino market rates, senior-heavy
 - **Cloud wins TCO in years 1–2; on-prem wins TCO from year 3+** — decision framework in F.6.4
- **The differentiators (D §1–§8)**

1. Bilingual UI + SMS/USSD for feature-phone users
2. Offline-first PWA with CRDT sync (zero-loss under 72-h partition)
3. Self-hosted HR Copilot (Llama-3.1 / Qwen-2.5 in DepEd DMZ)
4. Payroll anomaly detector at the M6 parallel-run gate
5. Hash-chained audit ledger (Estonia X-Road pattern)
6. Public transparency portal (Georgia PSB pattern)
7. 10-year source escrow + community edition
8. Teacher-to-school placement optimiser (Chile SIGE pattern)

• **The top three risks (B \$15)**

1. **Payroll cutover data loss** — mitigated by the M6 parallel-run gate + statistical anomaly detector (D \$4)
2. **Regulator-triggered rework (CSC / DBM / BIR)** — mitigated by 90-day adaptation SLA + versioned rule engine
3. **Low-connectivity schools locked out** — mitigated by the offline PWA + CRDT sync (D \$2)

The 24-month plan

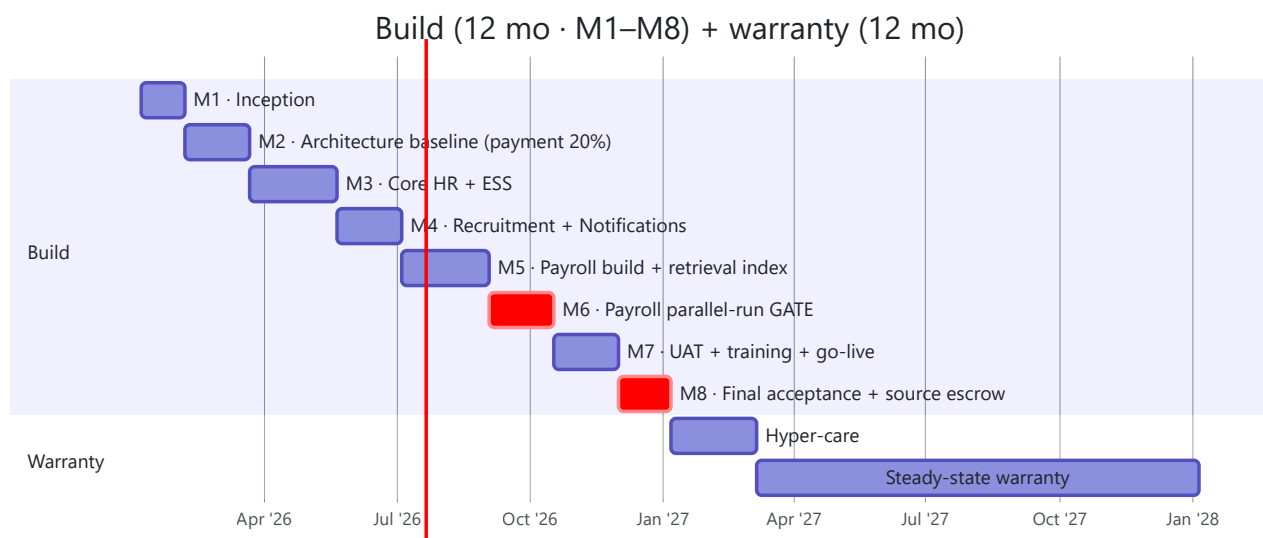

Where to go for detail

Question	Read
What does the PBD actually ask for?	Paper A · Brief
How do we answer it clause by clause?	Paper B · Response
What does the system look like?	Paper C · Architecture
How do we win vs. competitors?	Paper D · Value-Adds
Where's the international precedent?	Paper E · Benchmarks
Is PHP 500 M realistic?	Paper F · Delivery & Cost
How do we move 1 M records from legacy?	Paper H · Data Migration
How do we satisfy RA 10173 / NPC?	Paper I · Privacy Impact Assessment

Prepared as an independent analysis. Not affiliated with DepEd. Every figure is verifiable in the referenced paper. Full source at github.com/DennisPitallano/deped-hris-analysis.
